



**RIB LAKE**  
SCHOOL DISTRICT

# RIB LAKE SCHOOL DISTRICT EXECUTIVE SUMMARY

PROVIDED BY FINDORFF

1200 North Street • Rib Lake, WI 08.08.2025

## What's Happening?


As we count down the days until the teachers return to their classrooms, work at the Rib Lake School District continues to push forward. The new middle school locker rooms and restrooms have received paint, ceiling grid, and will have completed epoxy flooring very soon. The remainder of the middle school has been receiving finishes to allow for turnover in the next few weeks.

The addition work continues as well. The ironworkers have been hard at work setting the long span, and corridor joists, which have been followed by roof decking. When the steel roof work completes, the precast supports will be removed and preparation for the gym floor slab will begin.

In the high school, work has begun to wrap up inside of the wood shop as the mechanical and electrical contractors finish up their installations. The corridors throughout the building are receiving their new ceiling grid and tile, while the library has started to get put back together, as a temporary lunchroom.



The north addition vestibule CMU and structural steel have been completed.

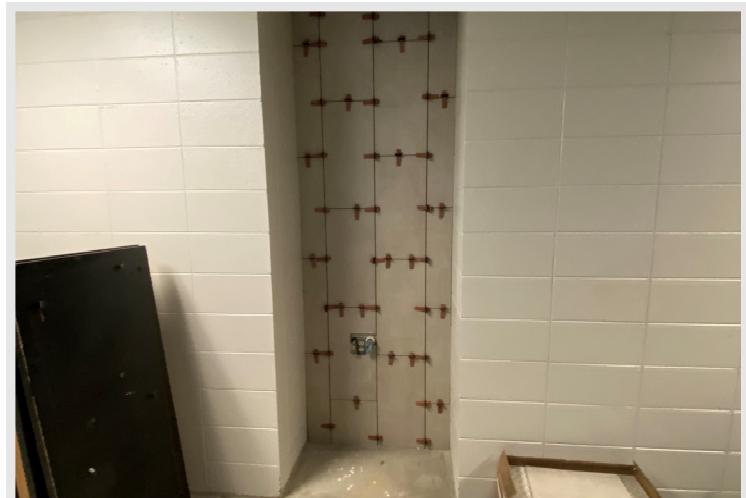

The wall tile behind the existing middle school water fountain has been installed.

## DID YOU KNOW?

Acoustical ceiling tiles bring many positives along with a clean appearance. Acoustical ceiling tiles also provide benefits in improved acoustics, better insulation, and access to the systems that are installed above them.

## Questions?

Project Manager, Ryan Treichel / 414.323.0611 / [rreichel@findorff.com](mailto:rreichel@findorff.com)

Superintendent, Jeremy Rosenthal / 608.287.8083 / [jrosenthal@findorff.com](mailto:jrosenthal@findorff.com)

**Findorff**  
BUILDING & BEYOND




**RIB LAKE**  
SCHOOL DISTRICT

# RIB LAKE SCHOOL DISTRICT EXECUTIVE SUMMARY

PROVIDED BY FINDORFF

1200 North Street • Rib Lake, WI PAGE 2

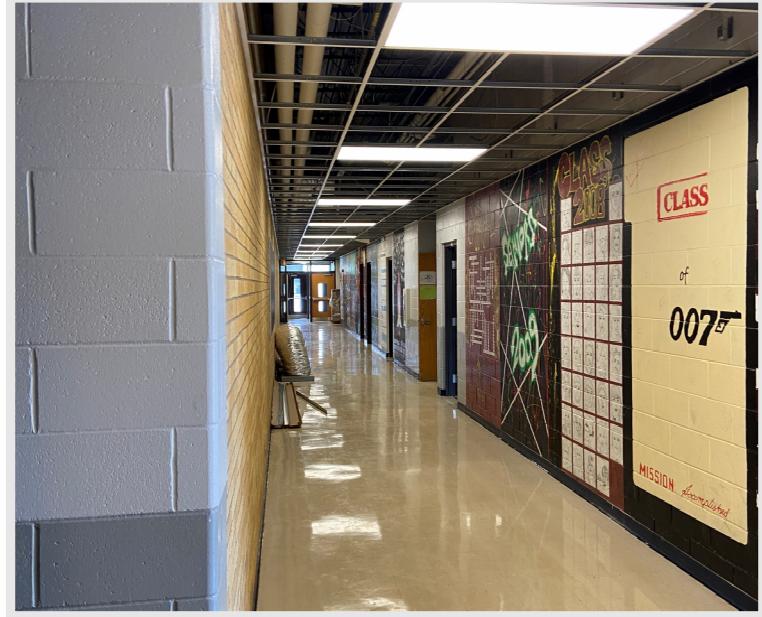

The epoxy flooring and cove base have been installed in the middle school locker rooms.

Ceiling grid and border are getting installed in the high school corridors.



The long span joists and roof decking have been installed above the new gym.

## Questions?

Project Manager, Ryan Treichel / 414.323.0611 / [rreichel@findorff.com](mailto:rreichel@findorff.com)

Superintendent, Jeremy Rosenthal / 608.287.8083 / [jrosenthal@findorff.com](mailto:jrosenthal@findorff.com)

**Findorff**  
BUILDING & BEYOND
